



## Southwest Quadrant Rehabilitation, City Project No. 20-002

Fiscal Year 2023-24, Quarter 3 (1/01/24 - 3/31/24)

Funding Source		Expenses	
City Funds	\$ -	Project Budget	\$ 1,646,927.50
Federal Funds		Encumbered	\$ 1,646,927.50
State Funds	\$ -	Total Expended	\$ 1,633,496.05
Measure L Funds	\$ 1,646,927.50	Available	\$ 13,431.45
<b>Total</b>	<b>\$ 1,646,927.50</b>		

### Project Details and Status:

City Council awarded the bid and approved an agreement in an amount of \$1,347,927.50 with George Reed, Inc. of Modesto, California, on June 13, 2023. The project includes different types of treatments on various roadways within the southwest quadrant of the City of Turlock. Construction is complete. Staff is working on Notice of Completion.

Completion Date: March 2024

Phase: Post Construction



Alaska Street



## Signal Coordination on W. Monte Vista Ave, Golden State Blvd, & Geer Rd, City Project No. 20-038

Fiscal Year 2023-24, Quarter 3 (1/01/24 - 3/31/24)


Funding Source		Expenses	
Federal Funds	\$ 254,375.00	Project Budget	\$ 348,375.00
State Funds		Encumbered	\$ 348,375.00
Measure L Funds	\$ 94,000.00	Total Expended	\$ 345,060.06
Other		Available	\$ 3,314.94
		Available from Measure L (Transfers yet to be done)	\$ 75,000.00
<b>Total</b>	<b>\$ 348,375.00</b>	Measure L Transfers (FY 21/22 & 22/23)	<b>\$ 19,000.00</b>

### Project Details and Status:

The project scope includes replacing the existing traffic signal controllers and installing new controllers that are capable of operating a signal timing plan. On August 9, 2022, City Council approved the contract with the low bidder, St. Francis Electric. Construction is complete and project is in the final close out phase.

Completion Date: March 2024

Phase: Post Construction

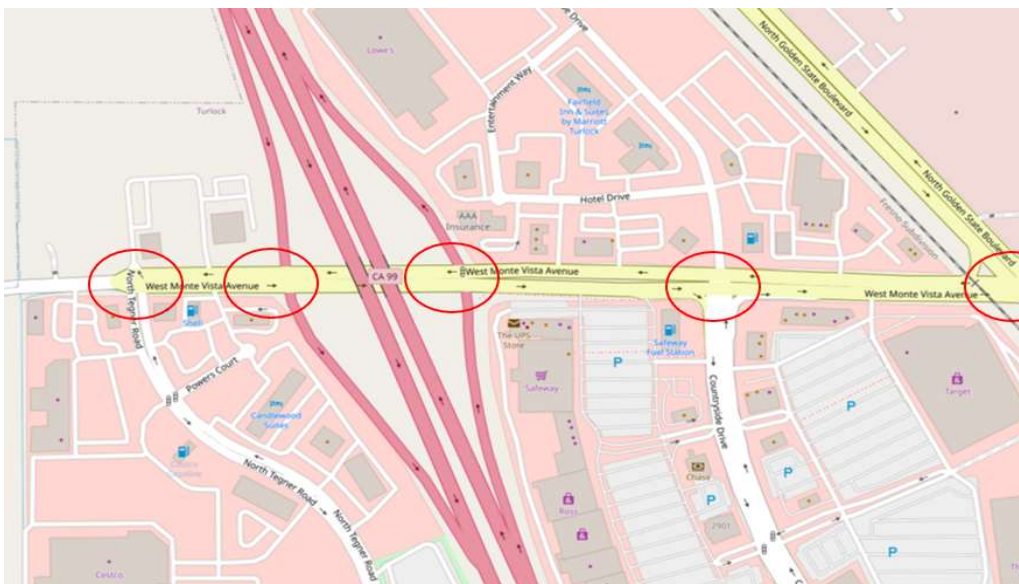

W. Monte Vista Ave intersection controller replacements



## Traffic Signal Synchronization on E. Monte Vista Avenue, City Project No. 20-039

Fiscal Year 2023-24, Quarter 3 (1/01/24 - 3/31/24)


Funding Source		Expenses	
Federal Funds	\$ 70,088.74	Project Budget	\$ 138,088.74
State Funds		Encumbered	\$ 138,088.74
Measure L Funds	\$ 68,000.00	Total Expended	\$ 81,807.72
Other		Available	\$ 56,281.02
<b>Total</b>	<b>\$ 138,088.74</b>	Measure L Transfers (FY 21/22 & 22/23)	<b>\$ 68,000.00</b>

### Project Details and Status:

This project will replace the existing traffic signal controllers and install new controllers that are capable of operating a signal timing plan. A signal coordination plan will help traffic signals operate more efficiently and reduce delay between signals on E. Monte Vista Avenue. On July 26, 2022, City Council awarded the contract to the lowest bidder, St. Francis Electric. Construction is complete and project is in the final close out phase.

Completion Date: March 2024

Phase: Post Construction

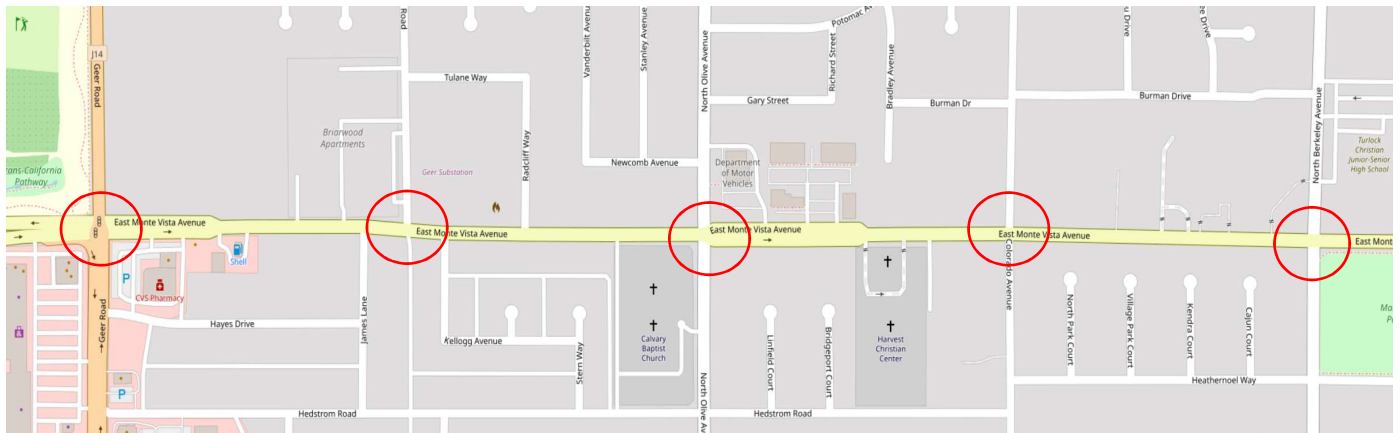





## Lander Avenue Rehabilitation, City Project No. 21-018

Fiscal Year 2023-24, Quarter 3 (1/01/24 - 3/31/24)

Funding Source		Expenses	
City Funds (Fund 420)	\$ 150,418.00	Project Budget	\$ 4,150,578.60
Federal Funds		Encumbered	\$ 4,150,578.60
State Funds	\$ -	Total Expended	\$ 3,999,849.55
Measure L Funds	\$ 4,000,160.60	Available	\$ 150,729.05
<b>Total</b>	<b>\$ 4,150,578.60</b>		

### Project Details and Status:

This project rehabilitated Lander Avenue between D Street and SR-99 and included vertical median with landscaping, new sidewalk, 18 access ramps, traffic signal loop replacements, and a pedestrian activated rectangular rapid flashing beacon crossing with pedestrian refuge. The contractor, George Reed Inc, was awarded the contract on August 9, 2022. Construction is complete.

Notice of Completion: October 24, 2023

Phase: Complete





## Pedras Road Rehabilitation, City Project No. 21-021

Fiscal Year 2023-24, Quarter 3 (1/01/24 - 3/31/24)

Funding Source		Expenses	
Federal Funds	\$ 873,883.00	Project Budget	\$ 1,903,356.29
State Funds	\$ -	Encumbered	\$ 1,903,356.29
Measure L Funds	\$ 1,029,473.29	Total Expended	\$ 120,767.13
Other		Available	\$ 1,782,589.16
<b>Total</b>	<b>\$ 1,903,356.29</b>	Measure L Transfers (FY 22/23)	<b>\$ 939,000.00</b>

### Project Details and Status:

The project will rehabilitate aged pavement on Pedras Road between Geer Road and Golden State Boulevard. It will include construction of accessible pedestrian ramps, removing a valley gutter and installing storm drain improvements, and placement of new traffic striping. Construction contract was awarded on September 26, 2023 to Sinclair General Engineering Construction. Construction will commence in April 2024.

Completion Date: June 2024

Phase: Pre-Construction



Pedras Rd



## Washington Rd Bridge Railing Repair, City Project No. 22-005

Fiscal Year 2023-24, Quarter 3 (1/1/24 - 3/31/24)

Funding Source		Expenses	
Federal Funds	\$ -	Project Budget	\$ 293,500.00
Measure L Funds	\$ 250,000.00	Encumbered	\$ 293,500.00
Other (SB 1)	\$ 18,500.00	Total Expended (Measure L)	\$ 61,124.49
Other (reimb)	\$ 25,000.00	Available	\$ 232,375.51
<b>Total</b>	<b>\$ 293,500.00</b>		

### Project Details and Status:

The bridge railing on the east side of Washington Road crossing over TID Upper Lateral No. 4 was destroyed by a vehicular accident in 2020. The project scope includes the removal of existing damaged northbound bridge railing, repair of damaged concrete decking, and installation of anchor plates, posts, railing, and traffic energy dissipator end treatment. City Council awarded the contract to Bugler Construction Inc. on the October 11, 2022, City Council meeting. Construction started in January 2023. Contractor has completed the punchlist items, and the project is in close-out phase. Staff anticipates Notice of Completion within the next few months.

Completion Date:

Phase: Post Construction

